Rudolph and Sletten
Project # 2787-0

Lawrence Berkeley National Laboratory
The Molecular Foundry
Building 67 & 67A

Week Starting 01-26-04
4 week Rolling Schedule

ID	Task Name	Contr.	Dur	Start
1				1/30/04
2	Install access gate 66 (Closure)	McG Hester	1 d	~~1/23/04~~
3	Rock at lower area	McG Hester	2 d	2/4/04
4	Install BMP's as necessary	McG Hester	5 d	1/26/04
5	Demo Trees	McG Hester	3 d	2/11/04
6	Develop access road	McG Hester	6 d	1/23/04
7	**66 FA underground pco 8003**	**R&S**	**1 d**	**1/30/04**
8	Red concrete/Backfill	R&S	1 d	1/30/04
9	**Site work / Early Utilities**		**10 d**	**1/28/04**
10	Relocate (SD) @ cooling tower	MJB	1 d	1/30/04
11	temp sanitary sewer w/tank	MJB	4 d	1/28/04
12	Install SD north end of wall	MJB	2 d	2/2/04
13	Install SS line @ bldg.62	MJB	5 d	2/4/04
14	**Selective demolition**		**3 d**	**2/2/04**
15	Concrete Wall @ lower lot	McG Hester	3 d	2/2/04
16	**HPNG Install**		**3 d**	**1/28/04**
17	Install added valve & backfill	MJB	3 d	1/28/04
18	**Ground Grid**		**9 d**	**1/23/04**
19	Install new grounding wells	Contra Costa	6 d	1/23/04
20	Tie in new ground grid 66	Contra Costa	1 d	2/2/04
21	Tie in bldg 72	Contra Costa	5 d	1/28/04
22	Tie in new ground grid 72	Contra Costa	1 d	2/4/04
23	**Building 62 FH relocate (pending pco)**		**16 d**	**2/6/04**
24	Shutdown Notice to LBL FH@62	MJB	2 d	2/6/04
25	Procurement (materials)	MJB	6 d	2/10/04
26	FH Shutdown **/****	LBNL Fac	1 d	2/18/04
27	Pothole for existing utilities	MJB	1 d	2/18/04
28	Excavate/ cap ***	MJB	2 d	2/18/04
29	Relocate FH/bollards	MJB	2 d	2/19/04
30	Test and backfill ***	MJB	2 d	2/23/04
31	Rework road and parking lot ***	McG Hester	3 d	2/25/04
32				
33				

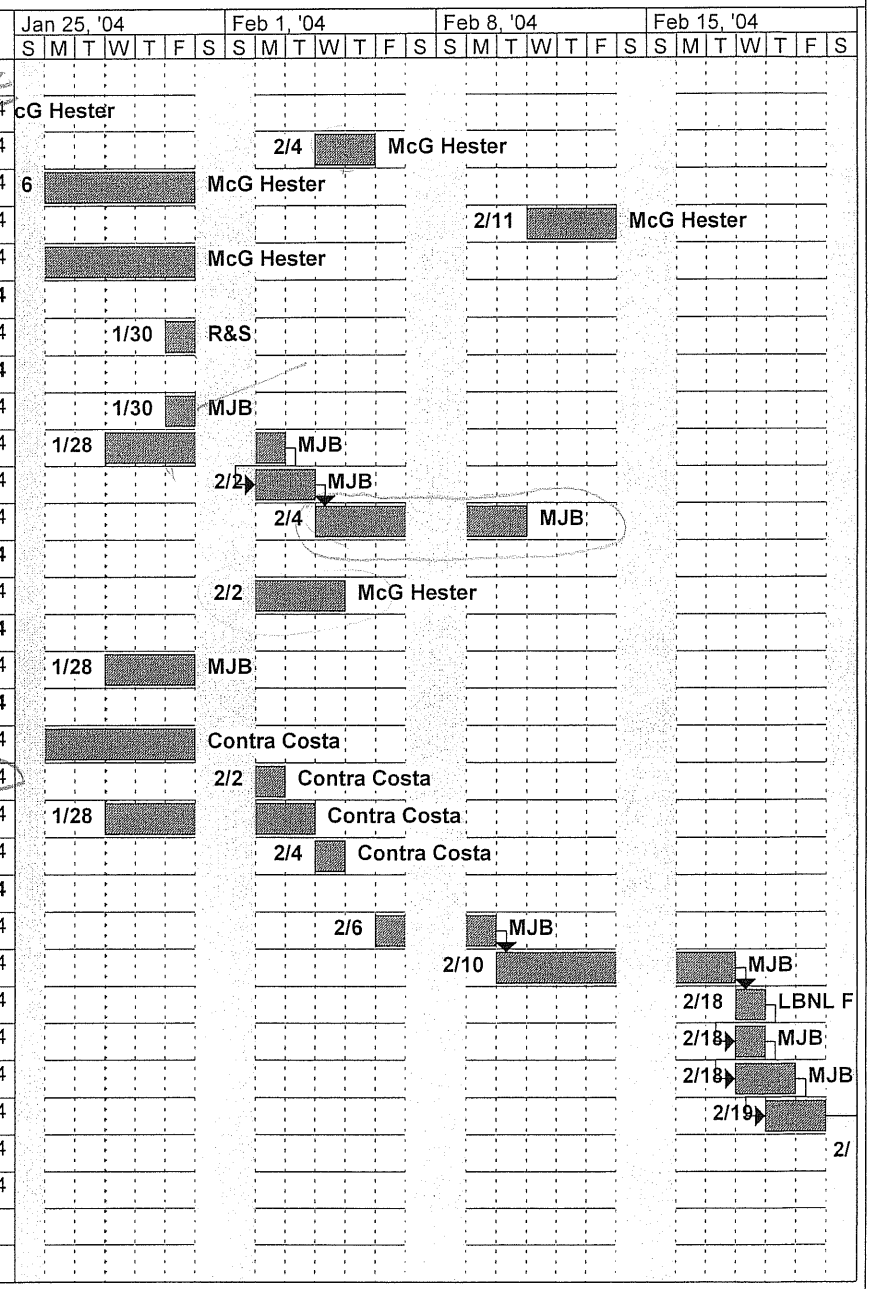

Rudolph and Sletten
Project # 2787-0

Lawrence Berkeley National Laboratory
The Molecular Foundry
Building 67 & 67A

Week Starting 01-26-04
4 week Rolling Schedule

ID	Task Name	Contr.	Dur	Start
34	**Building Excavation @ Shoring**		**18 d**	**1/26/04**
35	**#1 (822.00')**		**18 d**	**1/26/04**
36	Prelim ex for soldier beams **	McG Hester	5 d	1/26/04
37	Mobilize	DBM	3 d	1/28/04
38	Drill / install soldier beams M9-M41 **/***	DBM	4 d	2/2/04
39	install 3" shotcrete mud wall ***	DBM	3 d	2/4/04
40	Cure	DBM	1 d	2/6/04
41	bench / slope for balance of soldier beams	McG Hester	3 d	2/5/04
42	Drill / install balance of soldier beams **/***	DBM	9 d	2/6/04
43	**Tie Back Installation**		**52 d?**	**12/8/03**
44	**#2 (817.00')**		**52 d?**	**12/8/03**
45	Excavate bench **	McG Hester	3 d	2/9/04
46	Install Tiebacks ***	DBM	2 d	2/12/04
47	Install 3" shotcrete mud wall ***	DBM	3 d	2/16/04
48	Cure Concrete / Tension tiebacks ***	DBM	1 d	2/19/04
49				
50				
51				
52				
53				
54				
55				
56				
57				
58				
59				
60				
61				
62				
63				
64				
65	end		1 d?	12/8/03

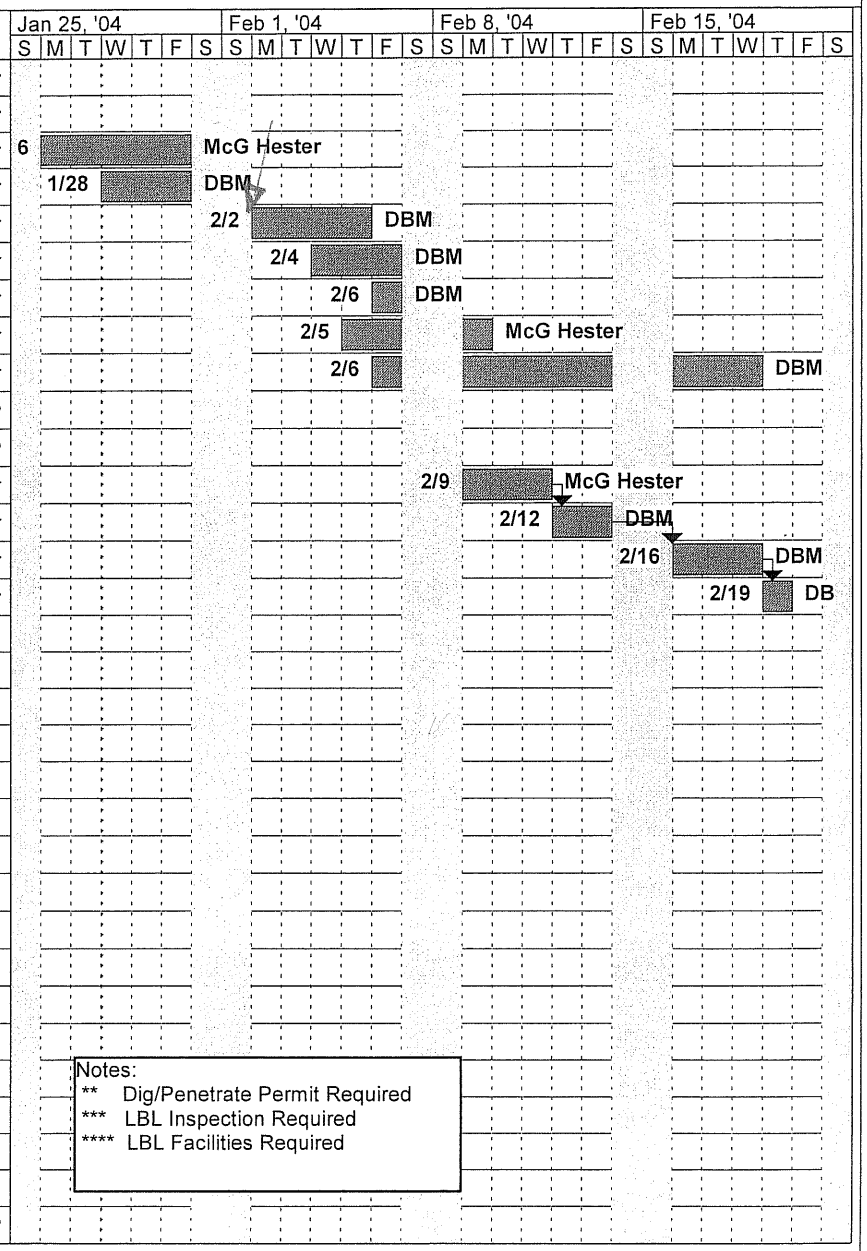

Notes:
** Dig/Penetrate Permit Required
*** LBL Inspection Required
**** LBL Facilities Required
