Rudolph and Sletten
Project # 2787-0

Lawrence Berkeley National Laboratory
The Molecular Foundry
Building 67 & 67A

Week Starting 06-21-04
4 week Rolling Schedule

ID	Task Name	Contr.	Dur	Start
1	**Mass Fill**		**177 d?**	**Mon 12/8/03**
2	offhaul excess	McG Hester	5 d	Mon 6/14/04
3	**Site work / Early Utilities**		**2 d**	**Thu 6/17/04**
4	Install SS line @ bldg.62 (pothole)	LBNL Fac	2 d	Thu 6/17/04
5	**Cooling Tower Shoring Wall**		**8 d**	**Mon 12/8/03**
6	#3 (790')		8 d	Mon 12/8/03
7	**Tie Back Installation**		**37 d?**	**Mon 6/14/04**
8	**failed wall m-41 thru m48**		**3 d**	**Thu 6/17/04**
9	excavate		2 d	Thu 6/17/04
10	shotcrete		2 d	Thu 6/17/04
11	Tension Tie Backs 3rd row		2 d	Fri 6/18/04
12	**(756.57")**		**3 d**	**Thu 6/17/04**
13	Excavate slots	McG Hester	1 d	Thu 6/17/04
14	Install shotcrete mud wall	DBM	1 d	Fri 6/18/04
15	Cure Concrete / Tension tiebacks	DBM	2 d	Fri 6/18/04
16	**Elevator # 2**		**4 d**	**Wed 6/16/04**
17	Excavate	McG Hester	1 d	Wed 6/16/04
18	Tie backs	DBM	1 d	Wed 6/16/04
19	Shotcrete	DBM	1 d	Thu 6/17/04
20	Stress Tie Backs	DBM	1 d	Mon 6/21/04
21	**Install Drilled Piers**		**23 d**	**Mon 6/21/04**
22	Mobilize		2 d	Mon 6/21/04
23	Line K & L 12 each	DBM	4 d	Wed 6/23/04
24	Line J, H, G 14 each	DBM	4 d	Tue 6/29/04
25	Line F, E 11 each	DBM	3 d	Mon 7/5/04
26	Line C, D 18 each	DBM	4 d	Thu 7/8/04
27	Line H/5 777' level 2 each	DBM	3 d	Wed 7/14/04
28	Stair Piers 814' level 2 each	DBM	3 d	Mon 7/19/04
29				
30				
31				
32				
33	**Temporary Electic Install**		**6 d?**	**Wed 6/16/04**

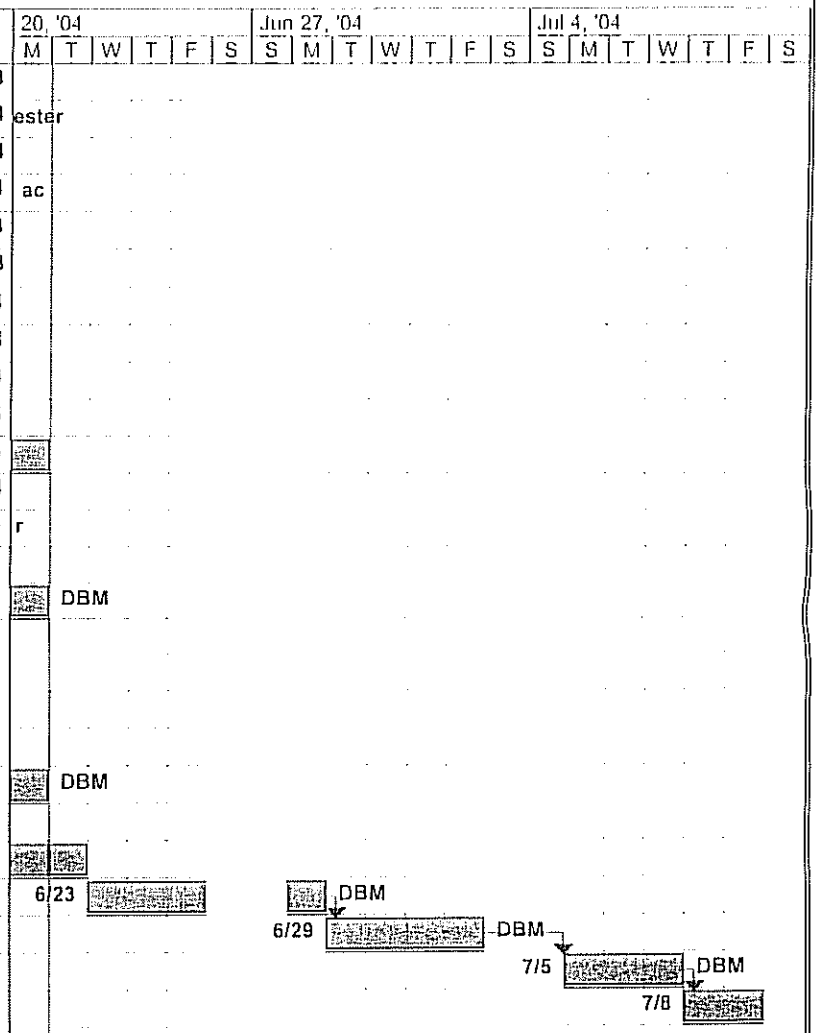

LBNL 4 week 06-14-04.mpp

Lawrence Berkeley National Laboratory

The Molecular Foundry

Building 67 & 67A
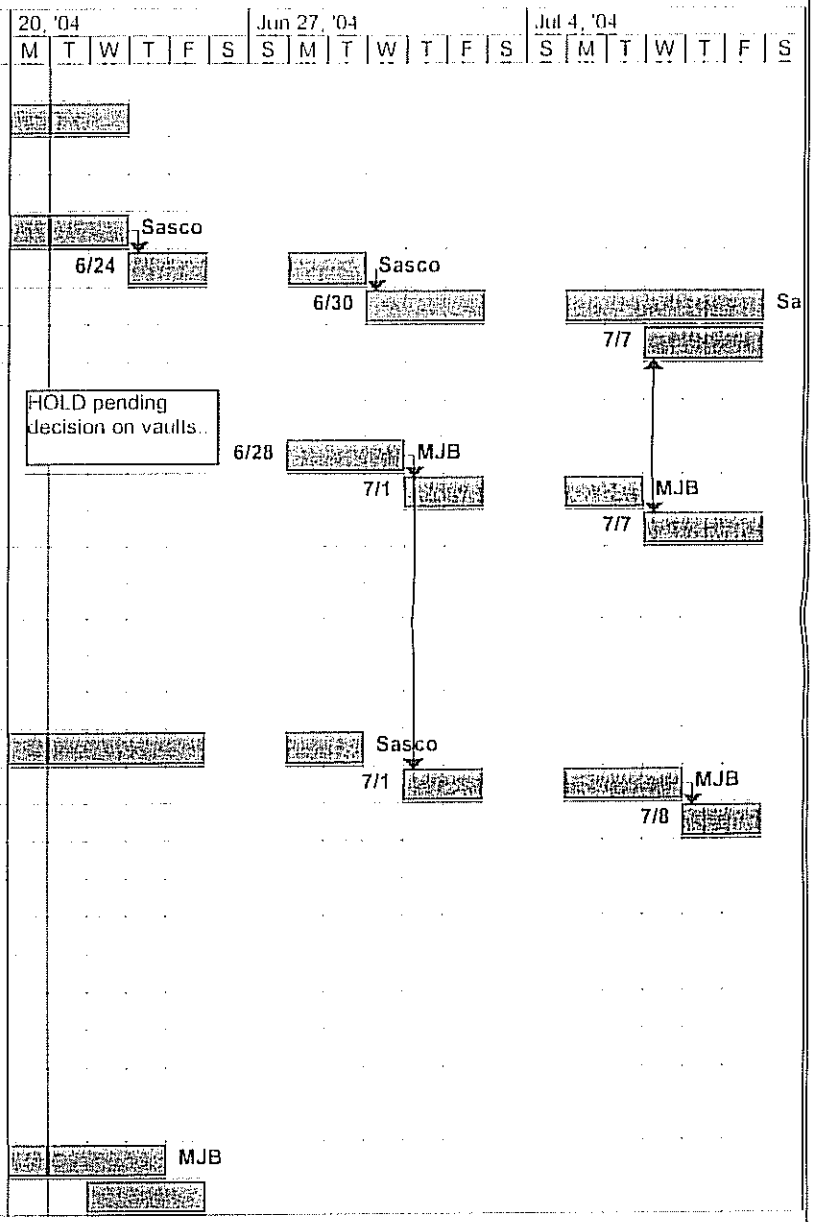
ID	Task Name	Contr.	Dur	Start
34	Temp Elec (shutdown @ 66)	Sasco	1 d?	Fri 6/18/04
35	Install temp Elec To 67		6 d	Wed 6/16/04
36				
37	**North Slope Utilities Install**		**26 d**	**Fri 6/18/04**
38	Manholes 227, 228	Sasco	4 d	Fri 6/18/04
39	Manholes 225, 226	Sasco	4 d	Thu 6/24/04
40	18 ea Conduit Duct Bank	Sasco	8 d	Wed 6/30/04
41	HPCW, HPNG	MJB	10 d	Wed 7/7/04
42	Storm Drain	MJB	8 d	Wed 7/14/04
43	**Lower fill area utilities**		**12 d**	**Mon 6/28/04**
44	Storm Drain	MJB	3 d	Mon 6/28/04
45	Head wall	MJB	4 d	Thu 7/1/04
46	V- Ditch / swale	BCI	5 d	Wed 7/7/04
47	**North Road A Utilities Install**		**4 d**	**Thu 7/15/04**
48	HPCW & HY 73	MJB	4 d	Thu 7/15/04
49	SS From Cooling Tower	MJB	3 d	Thu 7/15/04
50	**Road A Utilities Install**		**37 d**	**Mon 6/14/04**
51	Elect Vaults 223, 224	Sasco	4 d	Mon 6/14/04
52	Elect Duct Bank	Sasco	8 d	Fri 6/18/04
53	SS	MJB	5 d	Thu 7/1/04
54	Storm Drain	MJB	5 d	Thu 7/8/04
55	HPNG	MJB	4 d	Wed 7/21/04
56	HPCW	MJB	4 d	Thu 7/22/04
57	PD	MJB	4 d	Mon 7/26/04
58	CA	MJB	4 d	Thu 7/29/04
59	**South Slope Utilities Install**		**3 d**	**Mon 6/14/04**
60	Demo 2ea.conc. duct bank TM584	McG Hester	2 d	Mon 6/14/04
61	Reroute Conduits TMH584A	CC Elect	1 d	Wed 6/16/04
62	**Lawrence Rd. Utilites Install**		**5 d**	**Mon 6/21/04**
63	SD	MJB	4 d	Mon 6/21/04
64	PD	MJB	3 d	Wed 6/23/04
