Rudolph and Sletten
Project # 2787-0

Lawrence Berkeley National Laboratory
The Molecular Foundry
Building 67 & 67A

Week Starting 07-12-04
4 week Rolling Schedule

ID	Task Name	Contr.	Dur	Start	Finish
1			49 d?	Wed 6/23/04	Tue 8/31/04
2	**Install Drilled Piers**		21 d	Wed 6/23/04	Thu 7/22/04
3	Line K & L 12 each	DBM	4 d	Wed 6/23/04	Mon 6/28/04
4	Line J, H, G 14 each	DBM	4 d	Tue 6/29/04	Fri 7/2/04
5	Line F, E 11 each	DBM	3 d	Tue 7/6/04	Thu 7/8/04
6	Line C, D 18 each	DBM	4 d	Fri 7/9/04	Wed 7/14/04
7	Line H/5 777' level 2 each	DBM	3 d	Thu 7/15/04	Mon 7/19/04
8	Stair Piers 814' level 2 each	DBM	3 d	Tue 7/20/04	Thu 7/22/04
9	**Waterproofing 8' lift**		9 d	Fri 7/16/04	Wed 7/28/04
10	Picture framing on 1-line	Blues	4 d	Fri 7/16/04	Wed 7/21/04
11	L line	Blues	5 d	Wed 7/21/04	Tue 7/27/04
12	1 line	Blues	5 d	Wed 7/21/04	Tue 7/27/04
13	4 line	Blues	5 d	Thu 7/22/04	Wed 7/28/04
14	**Bldg. 67 Foundations 760'**		14 d	Fri 7/16/04	Wed 8/4/04
15	layout	Conco	2 d	Fri 7/16/04	Mon 7/19/04
16	Excavate	Conco	10 d	Mon 7/19/04	Fri 7/30/04
17	Rebar	Conco	8 d	Thu ~~7/22~~ 7/21/04	Mon 8/2/04
18	Underslab conduits	Sasco	3 d	7/19 Mon 7/19/04	Wed 7/21/04
19	Anchor Bolts	Conco	6 d	Tue 7/27/04	Tue 8/3/04
20	install embeds	Conco	2 d	Wed 7/28/04	Thu 7/29/04
21	Place Concrete	Conco	2 d	Fri 7/30/04	Mon 8/2/04
22	Temp Footing @ B line	Gayle	2 d	Tue 8/3/04	Wed 8/4/04
23	**Foundation Drain System**		4 d	Mon 7/26/04	Thu 7/29/04
24	pipe at pile caps/ grade beams	KDS	4 d	Mon 7/26/04	Thu 7/29/04
25	sleeves at grade beams	KDS	4 d	Mon 7/26/04	Thu 7/29/04
26	**Elevator # 2 concrete**		11 d?	Thu 7/22/04	Thu 8/5/04
27	excavate	Conco	2 d	Thu 7/22/04	Fri 7/23/04
28	slab & sump pit rebar	Conco	3 d	Fri 7/23/04	Tue 7/27/04
29	slab concrete	Conco	1 d?	Wed 7/28/04	Wed 7/28/04
30	Electrical	Sasco	1 d	Thu 7/29/04	Thu 7/29/04
31	Wall Rebar	Conco	3 d	Thu 7/29/04	Mon 8/2/04
32	Formwork	Conco	3 d	Mon 8/2/04	Wed 8/4/04
33	Place Concrete	Conco	1 d?	Thu 8/5/04	Thu 8/5/04

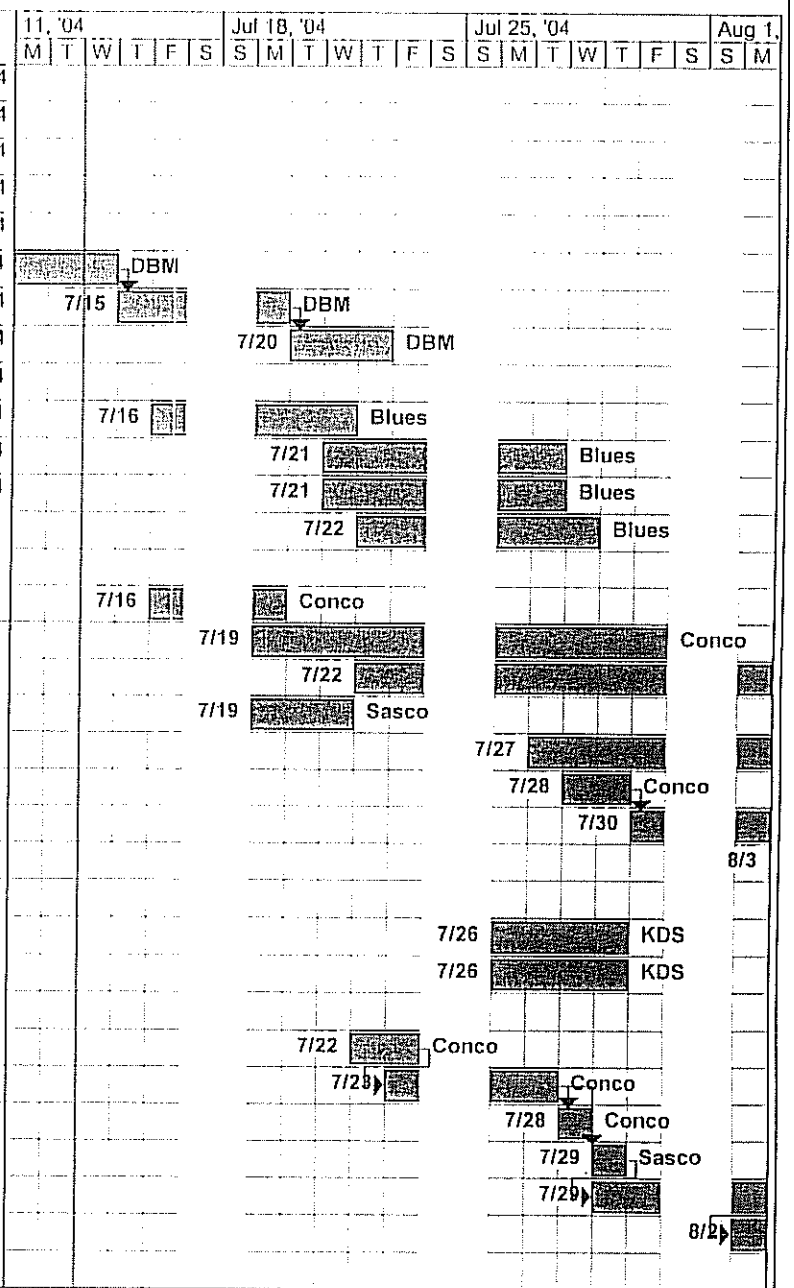

LBNL 4 week 07-12-04.mpp

ID	Task Name	Cont.	Dur	Start	Finish
34	**Elevator # 1 concrete**		11 d?	Thu 7/29/04	Thu 8/12/04
42	**Bldg. 67 Foundations 777'**		11 d	Mon 8/2/04	Mon 8/16/04
48	**Scaffold**		7 d	Tue 8/3/04	Wed 8/11/04
51	**Waterproofing**		18 d	Fri 8/6/04	Tue 8/31/04
54	**UB (67A) Foundations**		1 d?	Mon 8/2/04	Mon 8/2/04
56	**Cooling Tower Foundations**		1 d?	Mon 8/2/04	Mon 8/2/04
58	**Temporary Electic Install**		3 d	Thu 7/8/04	Mon 7/12/04
59	Install temp Elec To 67	Sasco	3 d	Thu 7/8/04	Mon 7/12/04
60	**Lower fill area utilities**		12 d	Wed 7/7/04	Thu 7/22/04
61	Storm Drain	MJB	3 d	Wed 7/7/04	Fri 7/9/04
62	Head wall	MJB	4 d	Mon 7/12/04	Thu 7/15/04
63	V- Ditch / swale	BCI	5 d	Fri 7/16/04	Thu 7/22/04
64	**Road A Utilities Install**		35 d?	Tue 7/6/04	Mon 8/23/04
65	Elect Duct Bank	Sasco	14 d	Tue 7/6/04	Fri 7/23/04
66	Elect Vaults 222	Sasco	2 d	Mon 7/19/04	Tue 7/20/04
67	Storm Drain	MJB	5 d	Tue 7/13/04	Mon 7/19/04
68	SS	MJB	5 d	Tue 7/20/04	Mon 7/26/04
69	HPNG	MJB	4 d	Tue 7/27/04	Fri 7/30/04
70	HPCW	MJB	4 d	Tue 7/27/04	Fri 7/30/04
71	PD	MJB	4 d	Mon 7/26/04	Thu 7/29/04
72	CA	MJB	4 d	Mon 8/2/04	Thu 8/5/04
73	Bulletin 19 work	MJB	4 d	Thu 7/22/04	Tue 7/27/04
74	**North end Road A Utilities Install**		8 d	Wed 7/21/04	Fri 7/30/04
75	HPCW & HY 73	MJB	4 d	Wed 7/21/04	Mon 7/26/04
76	SS From Cooling Tower	MJB	3 d	Wed 7/28/04	Fri 7/30/04
77	**North Slope Utilities Install**		33 d?	Thu 7/8/04	Mon 8/23/04
78	Manholes 227, 228	Sasco	0 d	Thu 7/8/04	Thu 7/8/04
79	Manholes 225, 226	Sasco	0 d	Thu 7/8/04	Thu 7/8/04
80	18 ea Conduit Duct Bank	Sasco	8 d	Mon 7/26/04	Wed 8/4/04
81	HPCW, HPNG	MJB	10 d	Thu 8/5/04	Wed 8/18/04
82	Storm Drain	MJB	8 d	Wed 8/11/04	Fri 8/20/04
83	install ground grid	Sasco	1 d?	Mon 8/23/04	Mon 8/23/04
84					

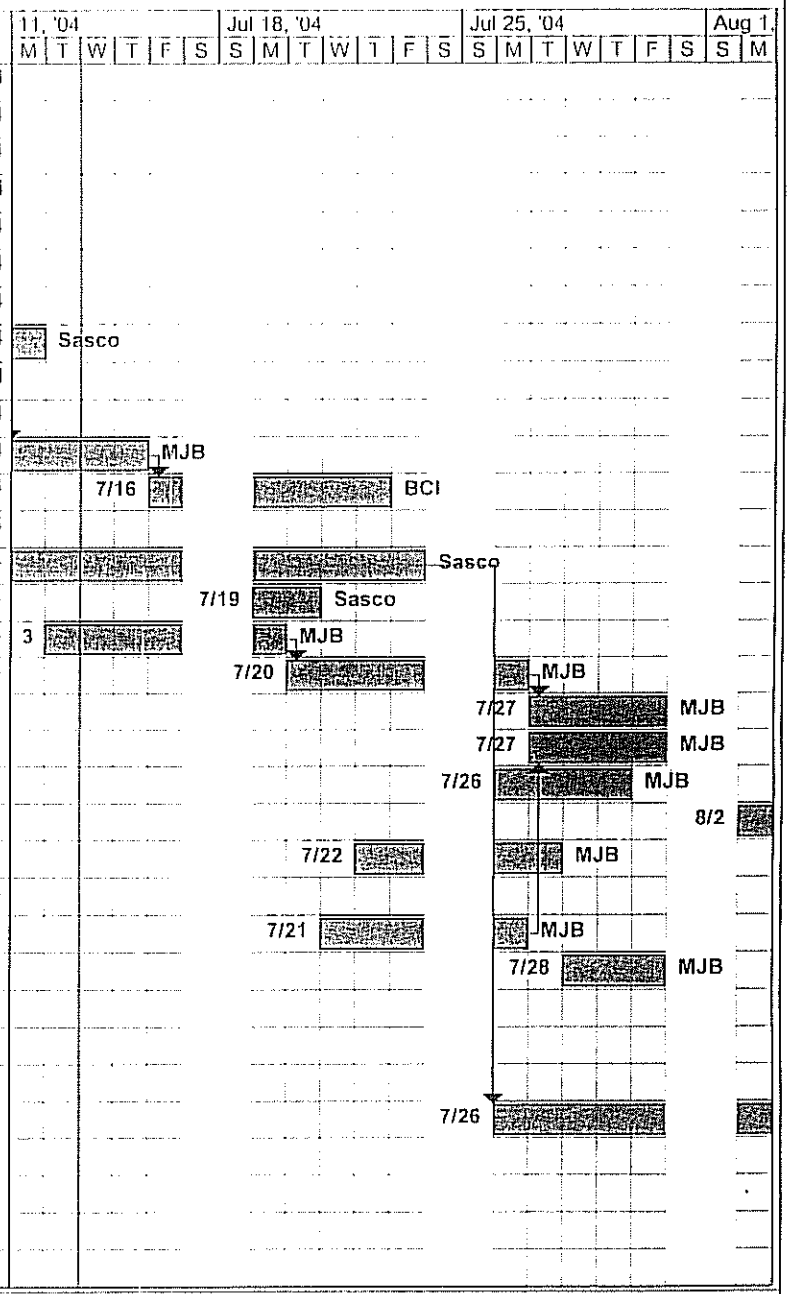
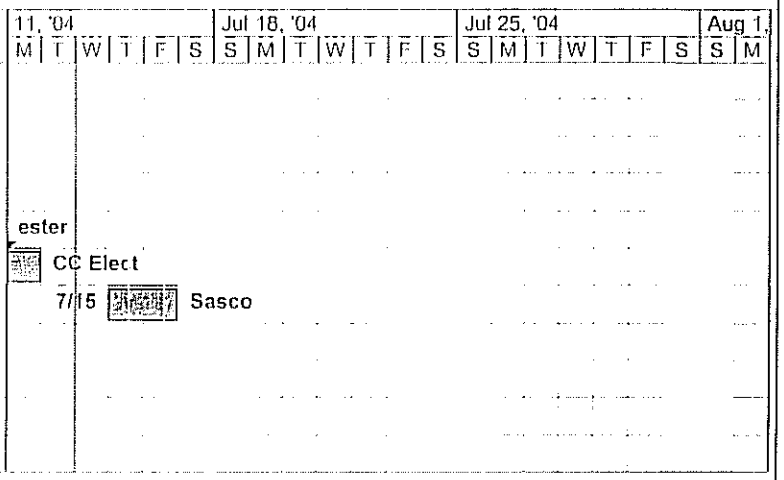
ID	Task Name	Contr.	Dur	Start	Finish
85					
86					
87					
88	**South Slope Utilities Install**		37 d?	Thu 7/8/04	Fri 8/27/04
89	repair conduit duct bank TM584	McG Hester	2 d	Thu 7/8/04	Fri 7/9/04
90	Reroute Conduits TM584A	CC Elect	1 d	Mon 7/12/04	Mon 7/12/04
91	Tele conduit 584a to 67	Sasco	2 d	Thu 7/15/04	Fri 7/16/04
92	SD & PD	MJB	4 d	Mon 8/23/04	Thu 8/26/04
93	install ground grid	Sasco	1 d?	Fri 8/27/04	Fri 8/27/04
94					
95	**Lawrence Rd. Utilites Install**		4 d	Mon 8/23/04	Thu 8/26/04
