Rudolph and Sletten
Project # 2787-0

Lawrence Berkeley National Laboratory
The Molecular Foundry
Building 67 & 67A

Week Starting 07-26-04
4 week Rolling Schedule

ID	Task Name	Contr.	Dur	Start	Finish
1			79 d?	Tue 6/1/04	Mon 9/20/04
2	**Install Drilled Piers**		3 d	Wed 7/28/04	Fri 7/30/04
3	Miscellaneous Clean Up Work	DBM	3 d	Wed 7/28/04	Fri 7/30/04
4	**Waterproofing 8' lift**		16 d	Fri 7/16/04	Fri 8/6/04
5	Picture framing on 1-line	Blues	4 d	Fri 7/16/04	Wed 7/21/04
6	L line	Blues	5 d	Wed 7/21/04	Tue 7/27/04
7	1 line	Blues	7 d	Wed 7/21/04	Thu 7/29/04
8	4 line	Blues	7 d	Thu 7/29/04	Fri 8/6/04
9	**Bldg. 67 Foundations 760' & 777'**		28 d	Fri 7/16/04	Tue 8/24/04
10	layout	Conco	2 d	Fri 7/16/04	Mon 7/19/04
11	Excavate	Conco	5 d	Mon 7/19/04	Fri 7/23/04
12	Edge Form	Conco	5 d	Tue 7/27/04	Mon 8/2/04
13	Place concrete L & 1 P2b to Elev. Pit	Conco	1 d	Fri 7/30/04	Fri 7/30/04
14	Rebar	Conco	5 d	Mon 8/2/04	Fri 8/6/04
15	Insert Collector pipe	KDS	2 d	Mon 8/9/04	Tue 8/10/04
16	Anchor Bolts	Conco	5 d	Wed 8/4/04	Tue 8/10/04
17	Place Concrete-On L Line to G.5	Conco	1 d	Wed 8/11/04	Wed 8/11/04
18	layout	Conco	2 d	Fri 7/23/04	Mon 7/26/04
19	Excavate	Conco	4 d	Wed 7/28/04	Mon 8/2/04
20	Edge Form	Conco	5 d	Tue 8/3/04	Mon 8/9/04
21	Rebar	Conco	4 d	Mon 8/9/04	Thu 8/12/04
22	Anchor Bolts	Conco	5 d	Thu 8/12/04	Wed 8/18/04
23	Insert Collector pipe	KDS	2 d	Tue 8/17/04	Wed 8/18/04
24	Place Concrete- Line K-/Line1-4	Conco	1 d	Thu 8/19/04	Thu 8/19/04
25	layout	Conco	2 d	Thu 7/29/04	Fri 7/30/04
26	Excavate	Conco	5 d	Fri 7/30/04	Thu 8/5/04
27	Edge Form	Conco	5 d	Wed 8/4/04	Tue 8/10/04
28	Rebar	Conco	5 d	Tue 8/10/04	Mon 8/16/04
29	Anchor Bolts	Conco	5 d	Tue 8/17/04	Mon 8/23/04
30	Insert Collector pipe	KDS	2 d	Fri 8/20/04	Mon 8/23/04
31	Install embeds	Conco	1 d	Fri 8/20/04	Fri 8/20/04
32	Place Concrete- Line G-C/Line1-4 & Line 5/C-H	Conco	1 d	Tue 8/24/04	Tue 8/24/04
33	Temp Footing @ B line	Gayle	1 d	Tue 8/24/04	Tue 8/24/04

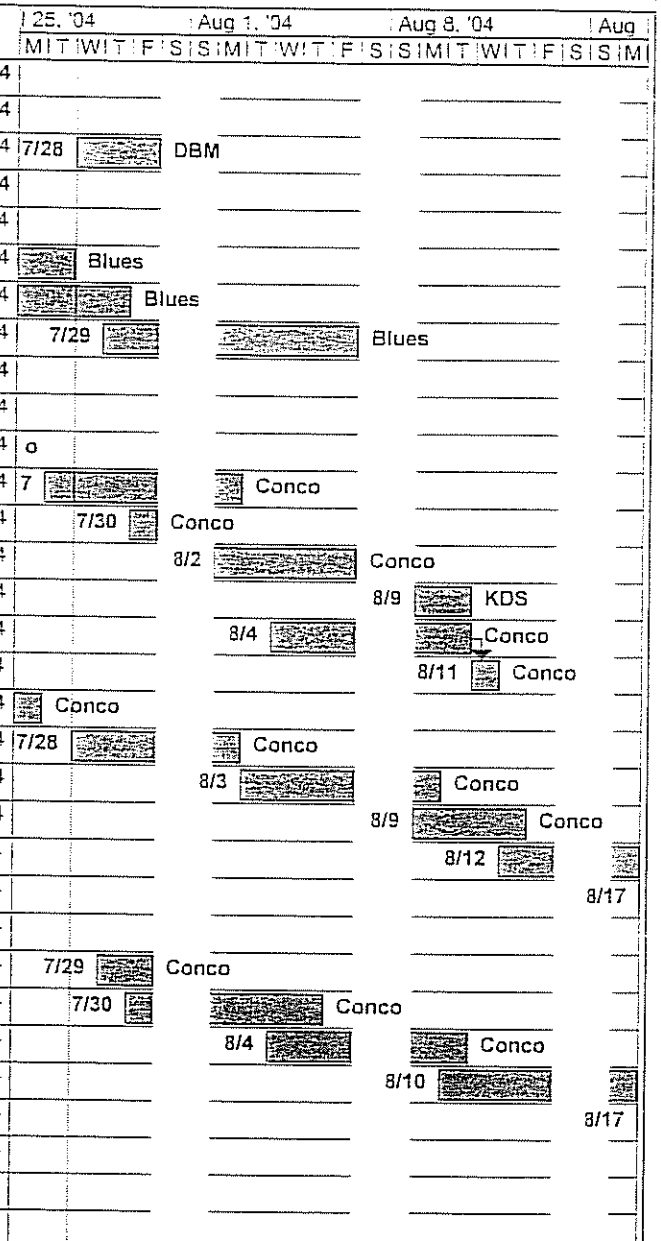

LBNL 4 week 07-26-04.mpp

ID	Task Name	Contr.	Dur	Start	Finish
34	**Foundation Drain System**		4 d	Mon 7/26/04	Thu 7/29/04
35	pipe at pile caps/ grade beams	KDS	4 d	Mon 7/26/04	Thu 7/29/04
36	sleeves at grade beams	KDS	4 d	Mon 7/26/04	Thu 7/29/04
37	**Elevator # 2 concrete**		11 d	Wed 7/28/04	Wed 8/11/04
38	slab & sump pit rebar	Conco	3 d	Wed 7/28/04	Fri 7/30/04
39	slab concrete	Conco	1 d	Fri 7/30/04	Fri 7/30/04
40	Electrical	Sasco	1 d	Mon 8/2/04	Mon 8/2/04
41	Wall Rebar	Conco	3 d	Mon 8/2/04	Wed 8/4/04
42	Formwork	Conco	3 d	Fri 8/6/04	Tue 8/10/04
43	Place Concrete	Conco	1 d	Wed 8/11/04	Wed 8/11/04
44	**Elevator # 1 concrete**		17 d	Mon 8/2/04	Tue 8/24/04
45	excavate	Conco	2 d	Mon 8/2/04	Tue 8/3/04
46	slab & sump pit rebar	Conco	4 d	Thu 8/5/04	Tue 8/10/04
47	slab concrete	Conco	1 d	Wed 8/11/04	Wed 8/11/04
48	Electrical	Sasco	1 d	Thu 8/12/04	Thu 8/12/04
49	Wall Rebar	Conco	3 d	Fri 8/13/04	Tue 8/17/04
50	Formwork	Conco	3 d	Wed 8/18/04	Fri 8/20/04
51	Place Concrete	Conco	1 d	Tue 8/24/04	Tue 8/24/04
52	**Scaffold**		8 d	Fri 8/20/04	Tue 8/31/04
55	**Waterproofing**		18 d	Thu 8/26/04	Mon 9/20/04
58	**UB (67A) Foundations**		15 d	Fri 7/30/04	Thu 8/19/04
59	Install Elec.	Sasco	4 d	Fri 7/30/04	Wed 8/4/04
60	Layout	Conco	1 d	Wed 8/4/04	Wed 8/4/04
61	Excavate	Conco	2 d	Thu 8/5/04	Fri 8/6/04
62	Install rebar	Conco	5 d	Mon 8/9/04	Fri 8/13/04
63	Install pipe collectors	KDS	1 d	Mon 8/16/04	Mon 8/16/04
64	Formwork	Conco	1 d	Tue 8/17/04	Tue 8/17/04
65	Templates for dowels	Conco	2 d	Tue 8/17/04	Wed 8/18/04
66	Pour Concrete	Conco	1 d	Thu 8/19/04	Thu 8/19/04
67	**Cooling Tower Foundations**		1 d?	Fri 8/6/04	Fri 8/6/04
68	Subgrade	Conco	1 d?	Fri 8/6/04	Fri 8/6/04
69	**Temporary Electic Install**		3 d	Thu 7/8/04	Mon 7/12/04
70	Install temp Elec To 67	Sasco	3 d	Thu 7/8/04	Mon 7/12/04

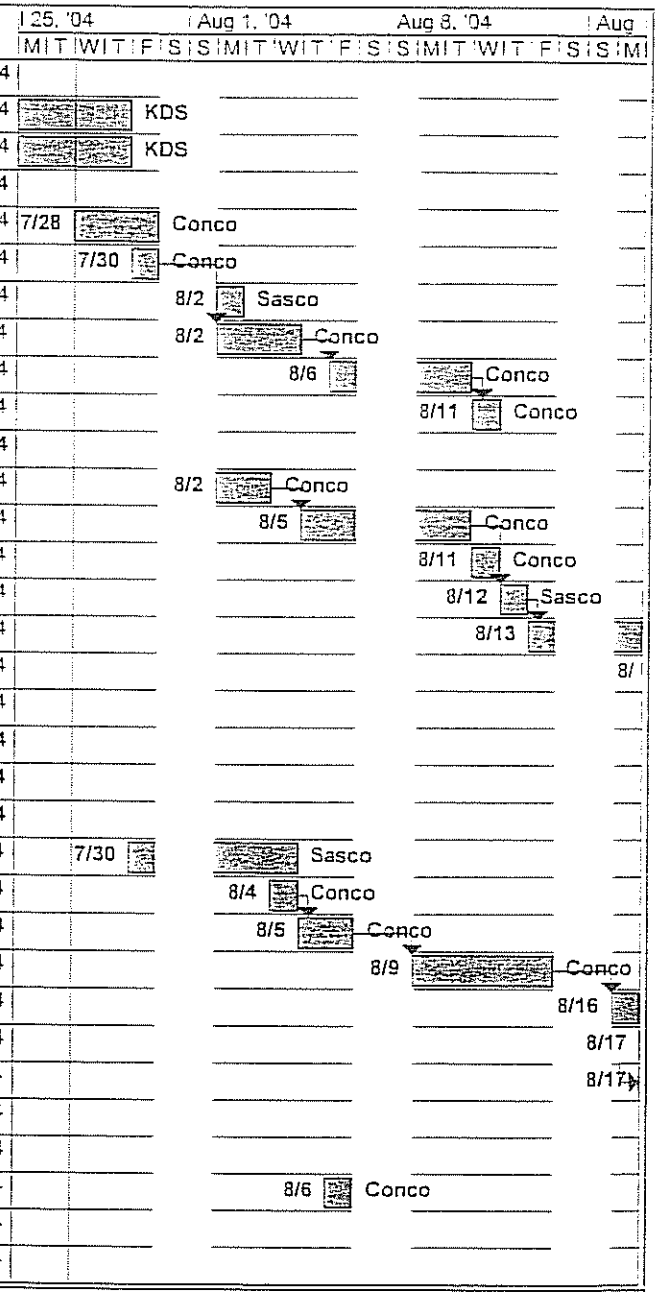
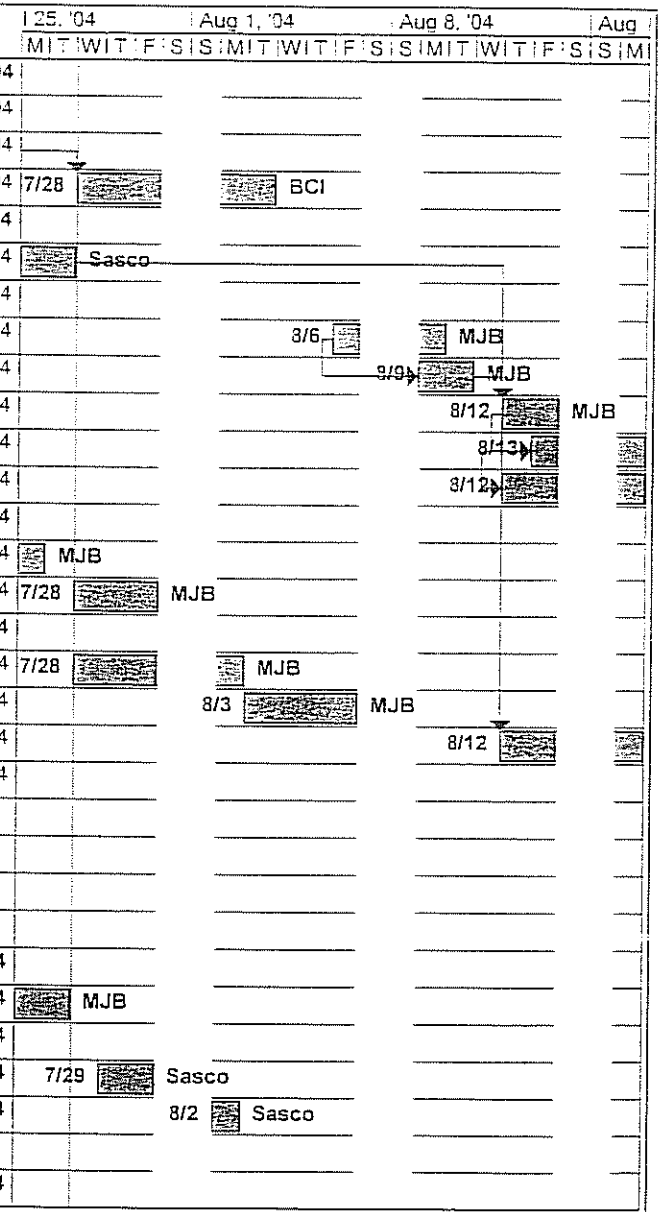
ID	Task Name	Contr.	Dur	Start	Finish
71	**Lower fill area utilities**		20 d	**Wed 7/7/04**	**Tue 8/3/04**
72	Storm Drain	MJB	3 d	Wed 7/7/04	Fri 7/9/04
73	Head wall	MJB	4 d	Mon 7/12/04	Thu 7/15/04
74	V- Ditch / swale	BCI	5 d	Wed 7/28/04	Tue 8/3/04
75	**Road A Utilities Install**		33 d?	**Thu 7/8/04**	**Mon 8/23/04**
76	Elect Duct Bank	Sasco	14 d	Thu 7/8/04	Tue 7/27/04
77	Elect Vaults 222	Sasco	2 d	Mon 7/19/04	Tue 7/20/04
78	HPNG	MJB	2 d	Fri 8/6/04	Mon 8/9/04
79	HPCW	MJB	2 d	Mon 8/9/04	Tue 8/10/04
80	PD	MJB	2 d	Thu 8/12/04	Fri 8/13/04
81	CA	MJB	2 d	Fri 8/13/04	Mon 8/16/04
82	Irrigation Sleeves Under Road	Shooter	3 d	Thu 8/12/04	Mon 8/16/04
83	**North end Road A Utilities Install**		8 d	**Wed 7/21/04**	**Fri 7/30/04**
84	HPCW & HY 73	MJB	4 d	Wed 7/21/04	Mon 7/26/04
85	SS From Cooling Tower	MJB	3 d	Wed 7/28/04	Fri 7/30/04
86	**North Slope Utilities Install**		19 d?	**Wed 7/28/04**	**Mon 8/23/04**
87	Storm Drain	MJB	4 d	Wed 7/28/04	Mon 8/2/04
88	HPCW, HPNG	MJB	4 d	Tue 8/3/04	Fri 8/6/04
89	18 ea Conduit Duct Bank	Sasco	8 d	Thu 8/12/04	Mon 8/23/04
90	install ground grid	Sasco	1 d?	Thu 8/19/04	Thu 8/19/04
91					
92					
93					
94					
95	**South Slope Utilities Install**		44 d?	**Tue 6/1/04**	**Mon 8/2/04**
96	SD & PD	MJB	4 d	Thu 7/22/04	Tue 7/27/04
97	Reroute Conduits TMH584A	CC Elect	1 d	Tue 6/1/04	Tue 6/1/04
98	Tele conduit 584a to 67	Sasco	2 d	Thu 7/29/04	Fri 7/30/04
99	install ground grid	Sasco	1 d?	Mon 8/2/04	Mon 8/2/04
100					
101	**Lawrence Rd. Utilites Install**		9 d	**Thu 7/29/04**	**Tue 8/10/04**
